



Smithtown Central School District

Athletic Field Renovations HS West

Fieldhouse Additions HS East & West

Fire Alarm Reconstruction HS West

Project Briefing : February 2023

Board of Education Update

March 6, 2023

Table of Contents

- a. Project Briefing
- b. Progress Photographs

Project Briefing March 6, 2022
Smithtown Central School District

Work completed in February 2023



Smithtown High School West Athletic Field Renovations
Varsity Softball Field & Varsity Baseball Field

- **Awaiting final turnover to district prior**




Smithtown High School East & West Field Houses

- Start and complete concrete flatwork and walkways
- Complete septic system and backfill (except formal startup)
- Start and complete roofing at West, start and continue roofing at East
- Prepare site for asphalt installation
- Start drywall ceilings (West)
- Upcoming work:
 - Weather permitting – Asphalt installation, soffit completion, start finishes, start flooring (West, weather permitting)



Smithtown High School West Final 10 13 2014

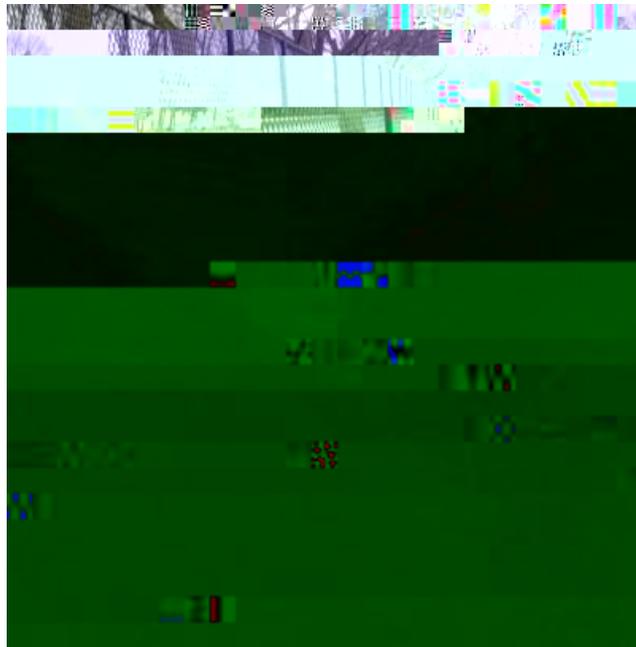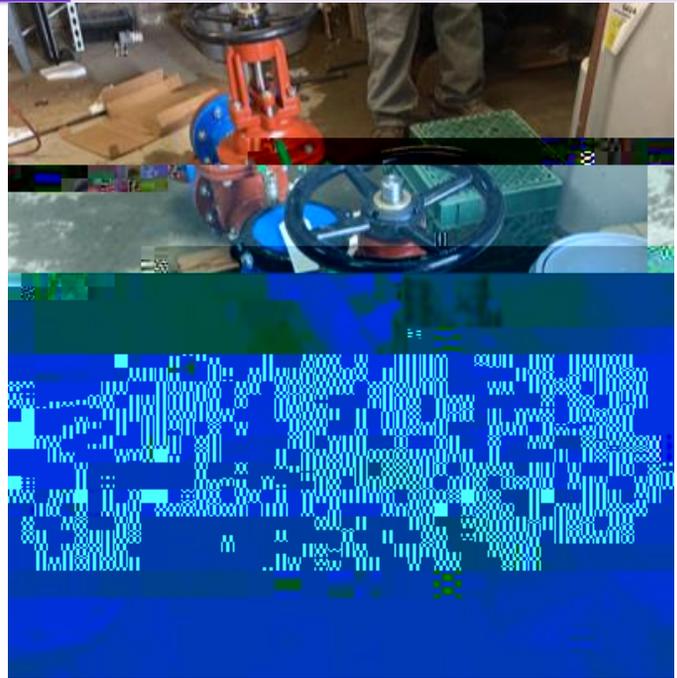

East Field House – Complete septic system and backfill, install new RPZ, install underground electric for bollard lighting

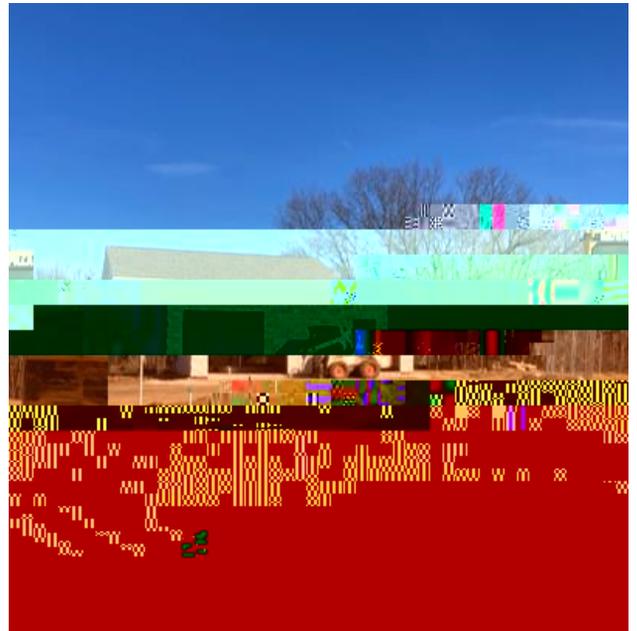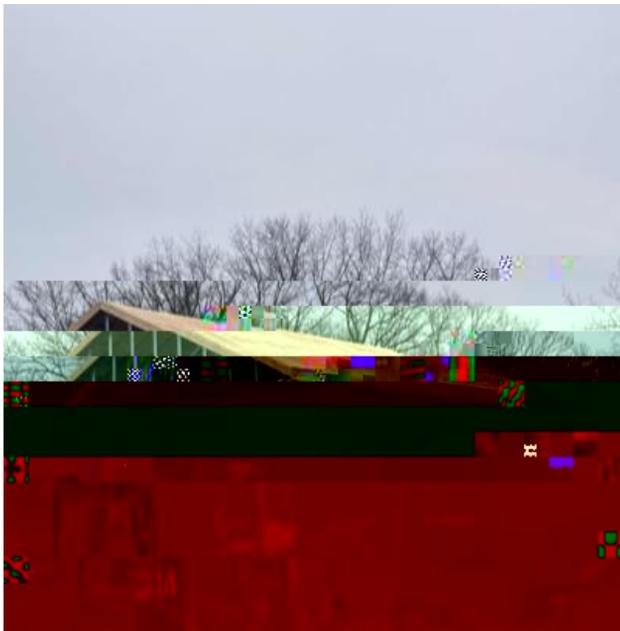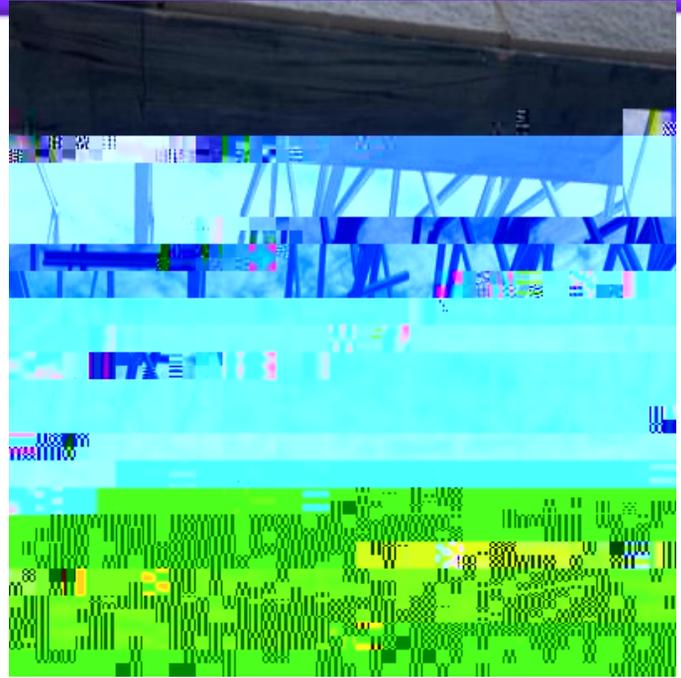

West Field House – Complete masonry, start and complete roof, finish septic system and backfill

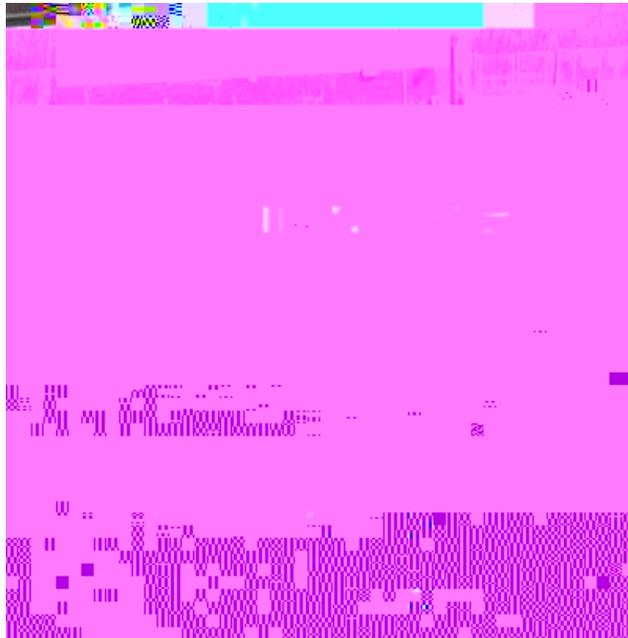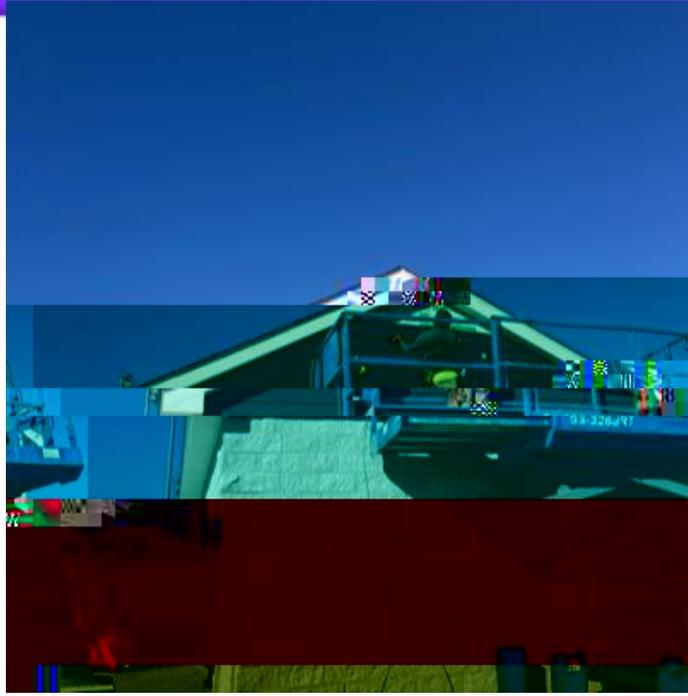

West Field House – Start and complete drywall ceilings, complete siding, prep subbase for asphalt,
